	Document No. PM-0004	Section No.
	Effective Date:	Revision No.
	PROCEDURAL MANUAL	
	DRAWING MANAGEMENT AND VERSION CONTROL	

OBJECTIVE	This procedure outlines the process for managing and controlling design drawings and other related documents within BHBI. It ensures that drawings are created, reviewed, approved, distributed, revised, stored, and retrieved in a systematic and controlled manner, using a consistent version control system. The aim is to ensure that all project stakeholders are working with the correct and latest approved drawings.
SCOPE	This procedure applies to all design drawings, specifications, and related documents created, received, or used by BHBI in the design and construction phases of its projects. This includes both electronic and hard copy drawings.

Responsibilities

- **Principal Designer:** Responsible for overseeing the creation, review, and approval of design drawings during the design phase. Also responsible for creating and revising the drawings.
- **Project Engineer:** Responsible for ensuring that the correct drawings are used during construction and that any drawing revisions are properly communicated and implemented on site.
- **Office Engineer:** Responsible for maintaining the drawing management system, controlling the distribution of drawings, tracking revisions, managing the drawing archive, and filing all project documents.
- **All Project Team Members:** Responsible for using the latest approved drawings and complying with this procedure.

Flowchart

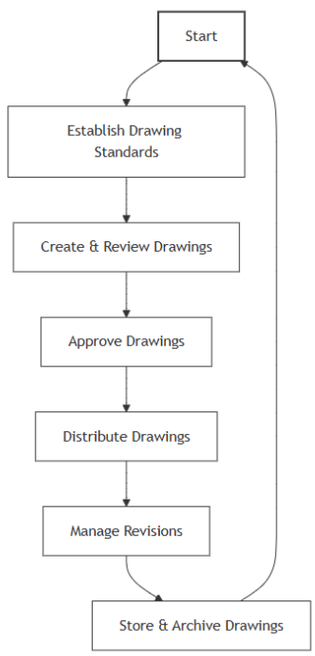

Procedure

4.1. Drawing Numbering and Identification:

- **Standard Numbering System:** Establish a standardized drawing numbering system that uniquely identifies each drawing. The system should include elements such as project number, discipline code, drawing type, sheet number, and revision number.
  - **Deliverables:** Drawing Numbering System Standard
- **Drawing Register:** The Office Engineer maintains a central drawing register or database that records all drawings, including their number, title, author, status, revision history, and location.
  - **Deliverables:** Drawing Register or Drawing Management System Database

4.2. Drawing Creation, Review, and Approval:

- **Drawing Templates:** Use standardized drawing templates to ensure consistency in format, title blocks, and other elements.
  - **Deliverables:** Drawing Templates
- **Drafting:** Drawings are created by the Principal Designer using approved CAD software.
- **Review:** Drawings are reviewed by the Project Engineer and other relevant stakeholders to ensure accuracy, completeness, compliance with codes and standards, and coordination between disciplines.
  - **Deliverables:** Review Comments
- **Revision:** The Principal Designer revises drawings based on review comments.
- **Approval:** Drawings are formally approved by the Principal Designer, indicating that they are ready for construction or the next stage of design.
  - **Deliverables:** Approved Drawings

4.3. Drawing Issuance and Distribution:

- **Controlled Distribution:** The Office Engineer is responsible for distributing approved drawings only to authorized personnel.
- **Transmittals:** Use formal transmittals to document the distribution of drawings, including the date, recipient, drawing numbers, revision numbers, and purpose of issue (e.g., "For Construction," "For Review").
  - **Deliverables:** Drawing Transmittals
- **Version Control:** Ensure that only the latest approved revision of a drawing is available for use. Clearly mark superseded drawings as "Superseded" or "Obsolete."

4.4. Drawing Revision and Control:

- **Revision Identification:** Clearly identify each revision of a drawing using a sequential revision number or letter (e.g., Rev. 0, Rev. 1, Rev. A, Rev. B).
- **Revision Block:** Update the revision block on the drawing to indicate the revision number, date, description of changes, and author of the revision.
- **Revision History:** The Office Engineer maintains a record of all revisions to each drawing in the drawing register, including the date, author, description of changes, and approval status.
- **Communication of Revisions:** The Office Engineer promptly communicates drawing revisions to all affected parties through formal transmittals.
- **Implementation of Revisions:** The Project Engineer ensures that drawing revisions are implemented on site and that superseded drawings are removed from circulation.

4.5. Drawing Storage and Retrieval:

- **Electronic Storage:** Store electronic drawings in a secure and organized manner on a central server or using a dedicated Electronic Document Management System (EDMS).
- **Hard Copy Storage:** If hard copy drawings are used, store them in a designated, secure, and organized location (e.g., plan room).
- **Retrieval:** Ensure that drawings can be easily retrieved when needed by authorized personnel.

4.6. Drawing Archiving:

- **Project Archive:** Upon project completion, the Office Engineer archives all project drawings according to the company's records retention policy.
    - **Deliverables:** Archived Project Drawings
- **Archive Index:** The Office Engineer maintains an index of archived drawings for easy retrieval.

4.7. Training:

- **Training Programs:** Provide training to all relevant personnel on drawing management procedures and the use of any drawing management systems.
    - **Deliverables:** Training Materials, Training Records

5. Continuous Improvement:

- Regularly review and update this procedure to incorporate lessons learned and improve the efficiency of drawing management and version control processes.

Records Generated (Deliverables)

- Drawing Numbering System Standard
- Drawing Register or Drawing Management System Database
- Drawing Templates
- Review Comments
- Approved Drawings
- Drawing Transmittals
- Archived Project Drawings
- Training Materials
- Training Records

This procedure should help BHBI manage its drawings effectively. Key elements include:

- **Clear Standards:** Defining standards for numbering, templates, and revisions.
- **Controlled Distribution:** Ensuring only approved drawings are used.
- **Version Control:** Tracking revisions and preventing the use of outdated drawings.
- **Secure Storage:** Protecting drawings from loss or damage.
- **Accessibility:** Making it easy to find and retrieve drawings when needed.

By consistently following this procedure, BHBI can reduce errors, improve project coordination, and maintain a reliable record of all project drawings.

Prepared by:	Reviewed by:	Approved by:	Noted by:
Marcone John Perea *Office Engineer*	**Mark Anthony Pajes** *Project Engineer*	**Nemesia P. Baylon** *Development Director*	**Adrian Carlo Escay** *President & CEO*
