	Document No.	Section No.
	Effective Date:	Revision No.
	PROCEDURAL MANUAL	
	SITE LOGISTICS AND PLANNING	

OBJECTIVE	This procedure outlines the process for planning and managing site logistics for BHBI construction projects. The aim is to ensure efficient and safe movement of materials, equipment, and personnel on site, optimize the use of site space, and minimize disruptions to construction activities.
SCOPE	This procedure applies to all BHBI construction projects and covers all aspects of site logistics, including site layout, access roads, traffic management, material storage, temporary facilities, security, and waste management. It starts from the project's mobilization phase and continues through to demobilization.

Responsibilities

- **Project Manager:** Overall responsibility for site logistics planning and implementation on their projects.
- **Project Engineer:** Responsible for developing and implementing the site logistics plan, in coordination with the Site Engineer.
- **Site Engineer:** Responsible for overseeing the day-to-day management of site logistics, including traffic flow, material storage, and site security.
- **Procurement:** Responsible for coordinating material deliveries with suppliers and ensuring timely arrival of materials.
- **Safety Officer:** Responsible for ensuring that the site logistics plan complies with all safety regulations and that site operations are conducted safely.
- **Subcontractors:** Responsible for complying with the site logistics plan and coordinating their activities with other trades.

Flowchart

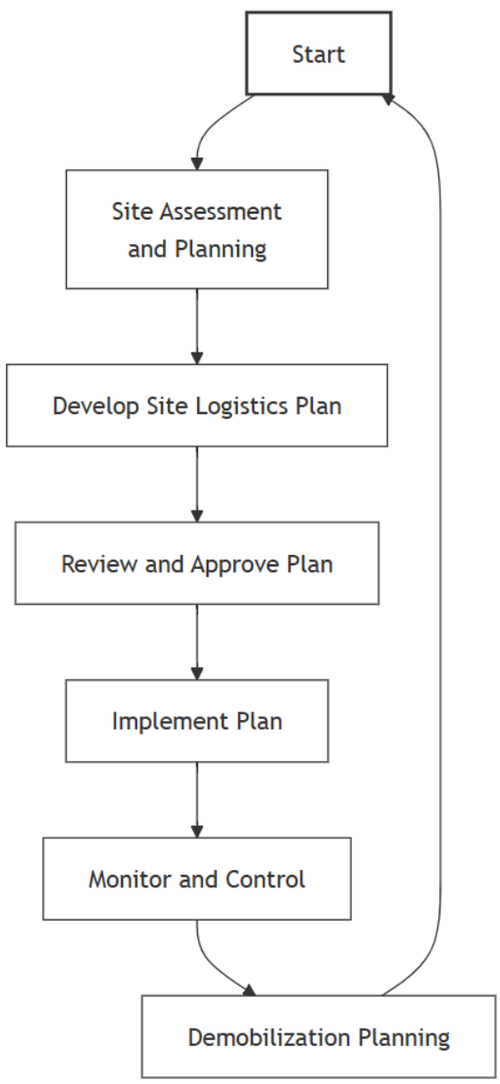

Procedure

4.1. Site Assessment and Planning:

- **Site Visit:** The Project Engineer and Site Engineer conduct a thorough site visit during the pre-construction phase to assess site conditions, identify potential constraints, and gather information for site logistics planning.
- **Information Gathering:** Collect and review relevant project documents, including:
  - Contract drawings and specifications
  - Project schedule
  - Construction methodology
  - Permits and approvals

- Local regulations (e.g., traffic restrictions, noise ordinances)

- **Develop Site Logistics Plan:** The Project Engineer, in collaboration with the Site Engineer, develops a detailed Site Logistics Plan that addresses the following:
  - **Deliverables:** Site Logistics Plan (This plan may be a drawing, a written document, or a combination of both).
  - The plan should include:
    - **Site Layout:** A drawing showing the site boundaries, access points, temporary roads, material laydown areas, location of temporary facilities (offices, toilets, etc.), parking areas, crane locations, and other key site features.
    - **Access and Egress:** Define site access and egress points for vehicles and pedestrians, considering traffic flow, safety, and security.
    - **Traffic Management:** Develop a traffic management plan to control the movement of vehicles and equipment on site, including designated routes, traffic control measures (e.g., signage, flaggers), and parking arrangements.
    - **Material Storage:** Designate areas for storing different types of materials, considering material handling requirements, proximity to work areas, and safety. (Refer to the *Material Storage and Handling Procedure*)
    - **Temporary Facilities:** Plan the location, size, and layout of temporary facilities, such as site offices, meeting rooms, welfare facilities, and storage sheds.
    - **Crane Locations:** Determine the optimal locations for cranes, considering lifting capacity, reach, and safety.
    - **Equipment Movement:** Plan the movement of heavy equipment on site, considering ground conditions, clearances, and safety.
    - **Security:** Develop a site security plan to prevent unauthorized access, theft, and vandalism.
    - **Waste Management:** Plan for the collection, storage, and disposal of construction waste.
    - **Perimeter Fencing and Signage:** Define the perimeter fencing requirements and signage for safety and security.
    - **Utilities:** Plan for temporary utilities (water, power, sanitation) needed during construction.

4.2. Plan Review and Approval:

- **Internal Review:** The Project Manager reviews and approves the Site Logistics Plan.
- **Client/Consultant Review (if required):** Submit the Site Logistics Plan to the client or their consultants for review and approval, if required by the contract.
- **Regulatory Approvals (if required):** Obtain any necessary approvals from local authorities for the Site Logistics Plan (e.g., traffic management plans).

4.3. Plan Implementation:

- **Site Setup:** The Site Engineer oversees the implementation of the Site Logistics Plan during the site mobilization phase. This includes setting up temporary facilities, establishing access roads, installing fencing and signage, and preparing material storage areas. (Refer to the *Mobilization and Pre-Project Activities Procedure*).
- **Communication:** Communicate the Site Logistics Plan to all project personnel, including subcontractors, suppliers, and other stakeholders.
- **Training:** Provide training to site personnel on traffic management, material handling, and other relevant aspects of the Site Logistics Plan.

4.4. Monitoring and Control:

- **Regular Inspections:** The Site Engineer conducts regular inspections to ensure that the Site Logistics Plan is being followed and that site operations are running smoothly and safely.
  - **Deliverables:** Site Inspection Reports
- **Plan Adjustments:** The Project Engineer and Site Engineer make necessary adjustments to the Site Logistics Plan in response to changing site conditions, construction progress, or unforeseen events.
- **Coordination Meetings:** Hold regular coordination meetings with subcontractors and suppliers to address any logistics-related issues.

4.5. Demobilization:

- **Plan for Demobilization:** As construction nears completion, the Project Engineer and Site Engineer develop a plan for demobilizing temporary facilities, removing equipment and materials, and restoring the site to its original condition. (Refer to the *Demobilization and Post-Project Activities Procedure*).

5. Safety:

- **Safety Procedures:** Integrate safety procedures into all aspects of site logistics planning and implementation.
- **Traffic Safety:** Emphasize traffic safety, particularly in areas with heavy vehicle and equipment movement.
- **Pedestrian Safety:** Provide safe pedestrian walkways and crossings on site.
- **Emergency Access:** Ensure that emergency vehicles have clear and unobstructed access to all parts of the site.

Records Generated (Deliverables)

- Site Logistics Plan
- Site Inspection Reports

Prepared by:	Reviewed by:	Approved by:	Noted by:
Marcone John Perea *Office Engineer*	**Mark Anthony Pajes** *Project Engineer*	**Nemesia P. Baylon** *Development Director*	**Adrian Carlo Escay** *President & CEO*
